BRHAT BANGALORE MAHANAGARA PALIKE
INSPECTION REPORT

Sl No	Decription	Details	Remarks
1	Name of Work	Improvements to Roads and Drains at Thirumenahalli to Chokkanahalli in ward no 05 Byataryanaprua sub Division	
2	Estimate Cost	19.99 Lakhs	
3	Administrative Approved No and Date	447/13-14, Date. 05.11.2013	
4	Technical sanction No. and Date	218/13-14, Date. 05.11.2013	
5	Job Code No. and P Code No.	005-13-000065	
6	Tender Direct Entrested to KRIDL	KRIDL	
7	if Tender, Tender Notification No. Date and Publication in daily news Paper	Not Applicable	
8	Tender Approved Details	Not Applicable	
9	Work Order No and Date	674/14-15, Date. 05.03.2014	
10	Stipulation time of Completion	60 Days	
11	Actiual Date of Commencement	16.05.2014	
12	Actiual Date of Completion	**10.11.2014**	
13	Delay if any	Nil	

14	Reson for Delay	Nil	
15	Payment made till date.	Nil	
16	Status of Work	Completed	
17	Photograph verfied	Enclosed	
18	Date of Inspection	25.06.2015	
19	BR NO. and Date	379/13.11.2014	
20	MB No. and Page No.	MB No,. 2573 Page No. 257219-31	
21	Test Result	Quality Test Report submitted by Civil tech Consultants and Engineer verified and Enclosed	
22	Section officer	Sri Chandrakanthraju P A AE	
23	Sub Division Office	Sri Shivakumar Goudar AEE Byatarayanaprua Sub Division	
24	Observation		
A	Work Quality	Satisfactory	
B	Comments	Work completed as per MB	

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ವ್ಯಾಪಾರಾಭಿವೃದ್ಧಿ ಇಲಾಖೆ ಯಲಹಂಕ ಸಂಚು
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ ಬೆಂಗಳೂರು-560 092.

25/06/15

Y C Kale gowda
Executive Engineer (Retd)

Name of work :- Improvements to Roads & Drains at Thirumenahalli to Chokkanahalli in Varanus Byatarayanapura Sub-Division

AE-05

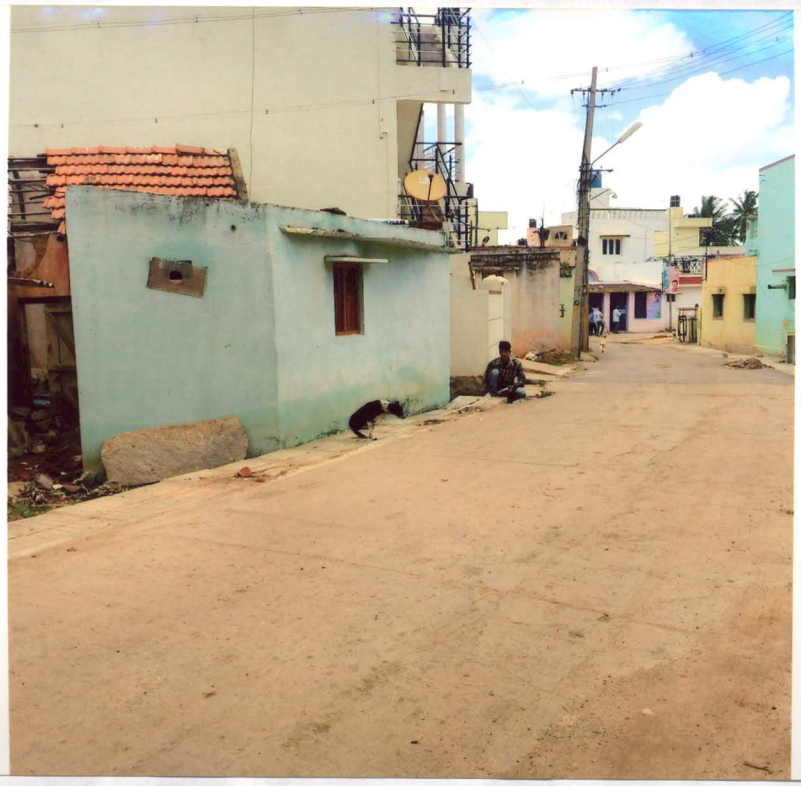

AEO

AE-05
